

**Implementation Status & Results
Cameroon
Environmental and Social Capacity Building for the Energy Sector (P109588)**

Operation Name: Environmental and Social Capacity Building for the Energy Sector (P109588) Project Stage: Implementation Seq.No: 8 Status: ARCHIVED Archive Date: 03-Apr-2013

Product Line: IBRD/IDA Country: Cameroon Approval FY: 2008
 Implementing Agency(ies): Region: AFRICA Lending Instrument: Specific Investment Loan

Key Dates

Board Approval Date	24-Jun-2008	Original Closing Date	31-Mar-2014	Planned Mid Term Review Date	19-Mar-2012	Last Archived ISR Date	11-Jun-2012
Effectiveness Date	28-Jan-2009	Revised Closing Date	31-Mar-2014	Actual Mid Term Review Date			

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The development objective of the project would be to: Improve the management of and the accountability for environmental and social issues related to large infrastructure investments, with an initial focus on the energy sector.

The Project would initially focus capacity building efforts towards the energy sector, in support of the Energy Sector Development Project. The mobilization of supplemental resources to more explicitly address issues in the mining and transport sectors would be explored during the project's mid-term review.

The expected long-term benefits of the project are to: (i) reduce the negative externalities of large infrastructure projects, and (ii) develop a transparent, stable and fair framework for managing environmental and social risks that should comfort large infrastructure investments, and (iii) institutionalizes information flows between the populations affected by large infrastructure projects and other stakeholders, and political decision-makers.

Has the Project Development Objective been changed since Board Approval of the Project?

Yes No

Component(s)

Component Name	Component Cost
Strengthening the Ministry in charge of the Environment	8.00
Establishing frameworks to manage social externalities	9.50
Supporting the Environment Unit in the Ministry of Energy and Water	2.50

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Unsatisfactory	Moderately Unsatisfactory
Overall Implementation Progress (IP)	Moderately Unsatisfactory	Moderately Unsatisfactory
Overall Risk Rating		

Implementation Status Overview

The Government of Cameroon and the Bank have been working on finalizing the process for the cancellation of the Project, following the request sent by the Government in February 2012. A work plan covering the period till end of June 2012 has been prepared by the Project, including mainly activities already started and which could be completed before end of June, as well as a limited number of capacity building activities.

All activities included in the workplan have been completed and delivered within the agreed time frame.

Locations

No Location data has been entered

Results

Project Development Objective Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Infrastructure projects in the energy sector approved that comply with int standards for environmental & social issues (KPI)	<input type="checkbox"/>	Percentage	Value	5.00	100.00	80.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments	percentage per annum	All large Energy Projects submitted to the Interministerial Committee received an Environmental Conformity Certificates.	
Energy sector facilities (existing) for which all enviromental & social impacts have been addressed (KPI)	<input type="checkbox"/>	Percentage	Value	5.00	50.00	80.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		Field missions to project sites were suspended since February 2012	
Facilities for which annual environmental performance report certified as compliant by MinEP with EMP (KPI)	<input type="checkbox"/>	Percentage	Value	10.00	30.30	70.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		24 facilities (21,87%) have imolemented their ESMPs in a satisfactory manner; 50 facilities (45,45%) have implemented the ESMP in amoderate way; while 15 facilities (13,63%) has an unsatisfactory performance.	

Domestic stakeholders with satisfactory understanding of norms and standards in matters of env & social diligence of large projects(KPI)	<input type="checkbox"/>	Percentage	Value	1.00	20.00	30.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		No data available beyond May 2012	

Intermediate Results Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Legislation on land management and compensation systems for involuntary resettlement adopted	<input type="checkbox"/>	Text	Value	NO		Yes
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		The procurement process stopped due to the cancellation request.	
EAs for new investments reviewed by Inter-Ministerial Committee (yearly)	<input type="checkbox"/>	Number	Value	54.00	80.00	45.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		No data available beyond March 2012.	
Energy sector facilities (existing) for which all environmental and social impacts have been identified through an audit process	<input type="checkbox"/>	Percentage	Value	0.00	13.00	80.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		No data available beyond March 2012.	
Sector guidelines on standards and procedural issues that integrate international best practices published	<input type="checkbox"/>	Number	Value	0.00	2.00	6.00
			Date	29-May-2008	30-Apr-2012	31-Mar-2014
			Comments		Only two guidelines were prepared. The remaining one is still under preparation.	
Pollution permits and licences issued	<input type="checkbox"/>	Number	Value	0.00	0.00	
			Date	29-May-2008	30-Apr-2012	31-Mar-2014
			Comments		The legislation doesn't cover pollution permits and licenses. This indicator was not be able to be reviewed at the MTR process, due to the early cancellation request.	
Non-compliance cases for which legal actions have been taken	<input type="checkbox"/>	Percentage	Value	0.00	50.00	80.00
			Date	29-May-2008	07-Jan-2012	31-Mar-2014
			Comments		Sur la base du rapport consolidé des missions d'inspections	

Public Disclosure Copy

					effectuées durant le mois de Mai 2012 à travers le pays, il ressort ce qui suit : 174 facilities have been inspected and 46 findings	
Policy to protecting and promoting the rights of marginal populations adopted	<input type="checkbox"/>	Text	Value	No		Yes
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		The hiring process of the consultant to prepare the draft policy stopped as a result of the project's cancellation.	Indicator not met as a result of the cancellation.
Reference health database developed (for selected reference sites)	<input type="checkbox"/>	Text	Value			
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		Reference data for the three main sites (Lom Pangar, Memvele and Kribi) still not shared by the Ministry of Health (considered confidential).	
Legal framework on cultural patrimony updated	<input type="checkbox"/>	Text	Value	No		Yes
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		Activity stopped following Project's cancellation	
Feedback comments/ questions about env/ social diligence provided monthly on the project website	<input type="checkbox"/>	Number	Value	0.00	20.00	50.00
			Date	29-May-2008	30-Apr-2012	31-Mar-2014
			Comments		The website design has been completed and operational .	
Audits (security, social, environmental) undertaken for existing infrastructure (annual)	<input type="checkbox"/>	Number	Value	0.00	26.00	100.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		Indicator not updated by the team.	
approved	<input type="checkbox"/>	Number Sub Type Breakdown	Value	0.00	24.00	100.00
			Date	29-May-2008	31-Dec-2011	
			Comments		Indicator not updated by the team.	
submitted	<input type="checkbox"/>	Number Sub Type Breakdown	Value	0.00	26.00	100.00
			Date	29-May-2008	31-Dec-2011	
			Comments		Indicator not updated by the team.	

Public Disclosure Copy

EMPs for large electricity infrastructure satisfactorily implemented	<input type="checkbox"/>	Percentage	Value	5.00	80.00	80.00
			Date	29-May-2008	07-Jan-2013	31-Mar-2014
			Comments		No updates provided by the team.	
SESA for the energy sector completed and disseminated	<input type="checkbox"/>	Text	Value	No		Yes
			Date		07-Jan-2013	31-Mar-2014
			Comments		Study is being prepared in the context of another Bank project (PDSEN) following cancellation of PRECESS.	

Data on Financial Performance (as of 05-Oct-2012)


Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P109588	IDA-44770	Effective	24-Jun-2008	30-Oct-2008	28-Jan-2009	31-Mar-2014	31-Mar-2014

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P109588	IDA-44770	Effective	XDR	12.30	12.30	0.00	4.62	7.68	38.00

Disbursement Graph

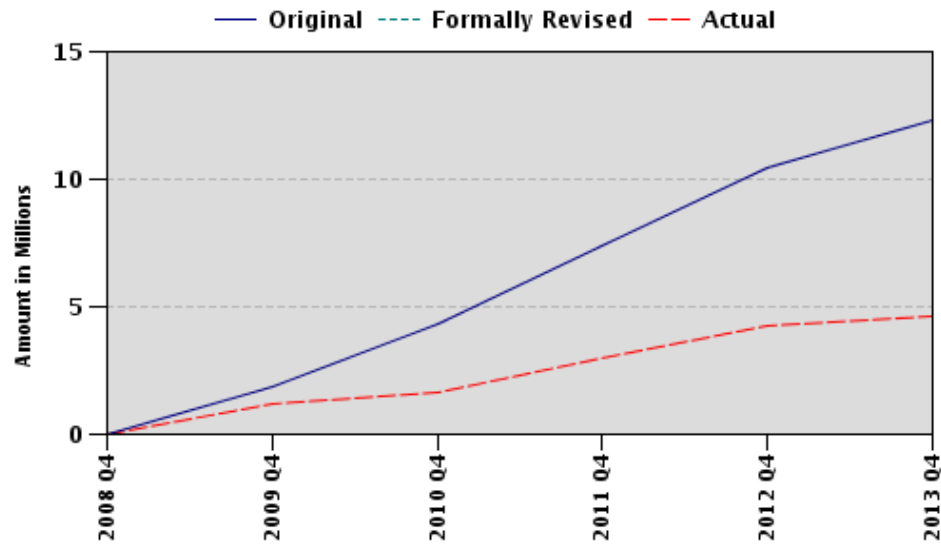

Key Decisions Regarding Implementation

All cancellation clearances have been granted.

Restructuring History

There has been no restructuring to date.

Related Projects

There are no related projects.
